INFRASTRUCTURE RENEWAL AT NEW YORK PENN STATION Program Milestone Report




Replace Track 15: January 5 to February 26	Activit	ty Status
Remove old rail and third rail	Complete	On Schedule
Remove old block ties	Complete	On Schedule
Remove old crossties and ballast	Complete	On Schedule
Demolition of concrete track bed	Complete	On Schedule
Install rebar and pour concrete track bed	Complete	On Schedule
Install block ties, rail and third rail	Complete	On Schedule
Install crossties, rail, third rail and ballast	Complete	On Schedule
Surface ballasted track	Complete	On Schedule
Install / test signal & power system	Complete	On Schedule
Paint platform	Complete	On Schedule
Rehabilitate Track 18: March 23 to May 14	Activit	ty Status
Drill holes for new plates		On Schedule
Remove old rail and third rail		On Schedule
Remove embedded tie plates & grout		On Schedule
Install new anchors & tie plates		On Schedule
Install rail & third rail		On Schedule
Replace #625 Turnout		On Schedule
Replace Additional Turnouts in "C" Interlocking	Activit	ty Status
Replace #641 Turnout March 2 to March 19		On Schedule
Replace #639 Turnout May 18 to May 28		On Schedule





INFRASTRUCTURE RENEWAL AT NEW YORK PENN STATION

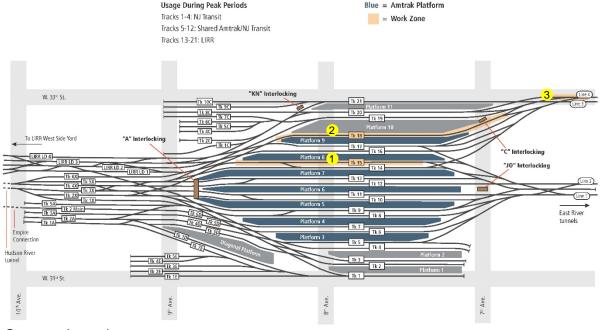

Source: Amtrak
